
Village of Arlington Heights

33 South Arlington Heights Road
Arlington Heights, Illinois 60005
847-368-5000
www.vah.com

Construction Fence / Silt Fence Acknowledgment

Both silt fences and construction fences must be installed and inspected prior to the start of work, when applicable. A 6-foot-tall chain-link construction fence with driven posts or sandbag-supported will be required. All fencing must be maintained in good condition throughout the duration of the project and removed upon final site stabilization, completion of work, and approval during the fence removal inspection.

1. **New Construction (Residential or Commercial)**
   - Required prior to any grading, excavation, or foundation work.
   - Silt fence prevents soil runoff into public right-of-way or storm drainage systems.
   - Construction fence secures the site for public safety and restricts unauthorized access.
2. **Additions or Major Alterations**
   - Required when ground disturbance occurs (e.g., digging footings, new foundation walls, exterior utility work, or re-grading).
   - Also needed if upper-story work creates a falling debris hazard (e.g., adding a second story on an existing house).
3. **Pools (In-ground or Large Above-ground)**
   - Both fences are required:
     - Silt fence for erosion control during excavation.
     - Construction fence for site safety and to prevent unauthorized entry.
4. **Commercial Site Work or Tenant Build-outs**
   - Typically required when exterior work includes grading, sidewalk installation, underground utilities, or façade renovations involving scaffolding.
5. **When Not Required (in practice)**
   - Minor work that doesn't disturb soil or pose public hazard concerns:
     - Roof, siding, or window replacements.
     - Sewer repair (short-term excavation may be managed with standard barricades)
     - Interior remodeling with no exterior exposure.
6. **Installation and Inspections**
   - At Installation: Engineering inspector will verify compliance for both silt and construction fences.
     - All fence footings must be placed entirely within the property lines of the construction site.

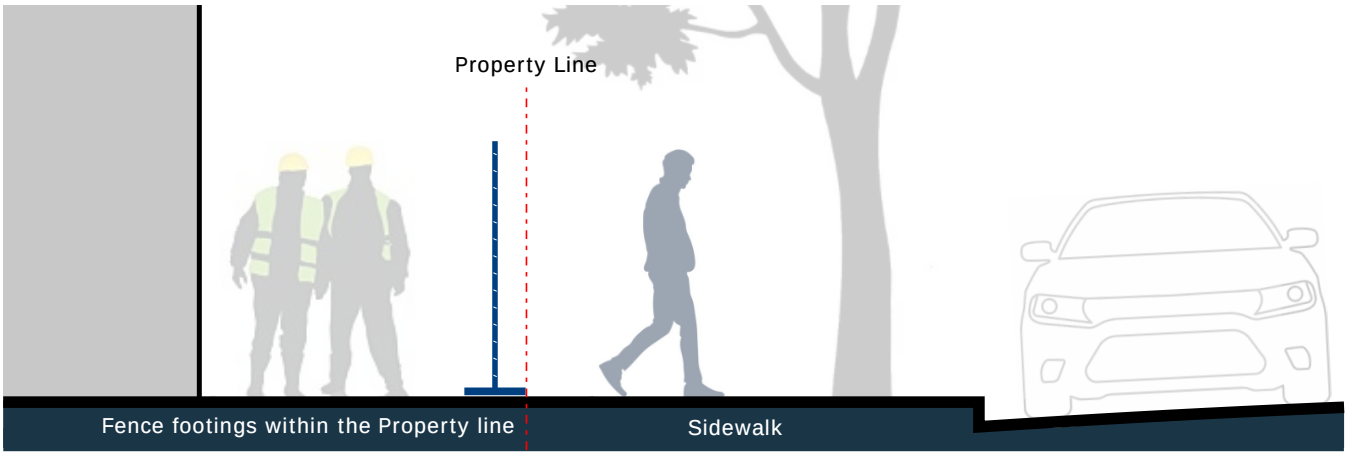


Village of Arlington Heights

33 South Arlington Heights Road
Arlington Heights, Illinois 60005
847-368-5000
www.vah.com

- At removal: Building inspector will verify compliance with the followings during fence removal:
  - All doors must be installed or properly boarded up.
  - Window well must be adequately covered.
  - Scaffolding must be removed.
  - No open trenches shall remain.
  - All construction materials and debris, including nails and trash containers, must be cleared from the site.

I acknowledge the requirements for construction fences and silt fences. The fences will be installed prior to any construction activities outlined above and will be inspected in accordance with the procedure described.

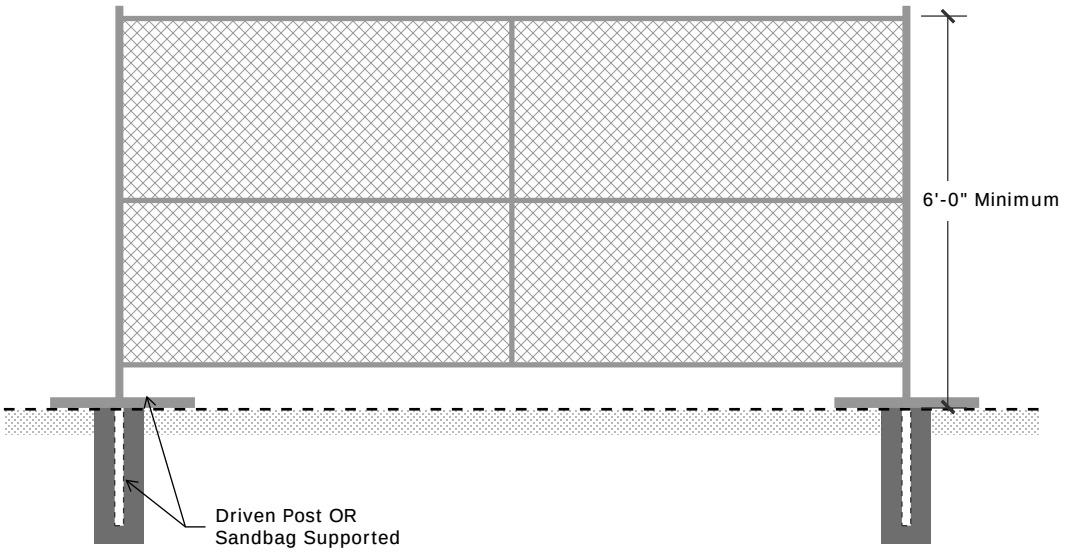

Job Address: _____ Permit Number: _____
Leave the permit number blank if it is not yet available

Print Name: _____ Signature: _____

Phone Number: _____ Date: _____

Drafted 12/1/2025
